


Commonwealth of Virginia IT Projects Status Report for May 2019 – Summary

Summary of the May 2019 Report - Category 1, 2, 3 Projects

| CIO Assessment | Number | Percent | Dollar Value | Percent |
|-----------------|--------|---------|---------------|---------|
| Active - Red | 4 | 12.5% | \$22,153,626 | 5.2% |
| Active - Yellow | 6 | 18.8% | \$141,347,215 | 33.4% |
| Active - Green | 21 | 65.6% | \$258,960,474 | 61.2% |
| Suspended | 1 | 3.1% | \$990,845 | 0.2% |
| Total | 32 | 100.0% | \$423,452,160 | 100.0% |

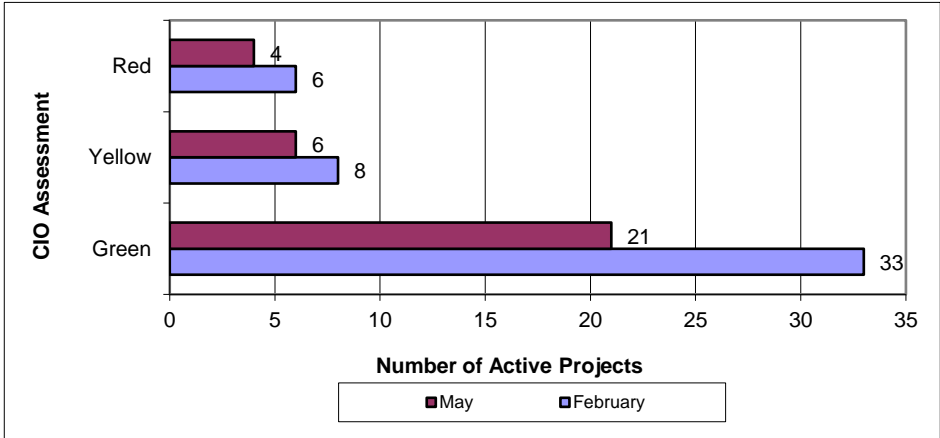

Commonwealth of Virginia IT Projects Status Report for May 2019 - Report Description

The report, organized by project life cycle phase, summarizes information as of the latest IT Project Status Reports submitted through ProSight, unless otherwise noted. The information includes the most recent agency rating of the Dashboard Key Status Indicators, CIO assessment and comment, and comments from the Auditor of Public Accounts (APA). The report is presented in three parts: Part 1 - Status Assessment and Comment; Part 2 - Baselines; Part 3 - Projected for Initiation Approval in the current quarter. Specific descriptions of the report contents are provided in the following notes.

Notes:

- (1) Secretariat and Agency identification numbers are now included in addition to the name.
- (2) Pre-ITIB denotes a project approved prior to the inception of the IT Investment Board on July 1, 2003.
- (3) Key Status Indicators:
 - Performance: Is the project on track to meet planned business goals and the associated measures of success?
 - Budget: Are the costs within the planned budget?
 - Schedule: Is the project on schedule?
 - Scope: Does the project remain within the approved scope?
 - Risk: Is the project being managed to minimize or mitigate the identified risks?
- (4) Ratings:
 - Green - On Track.
 - Yellow - Warning, consider corrective action or monitor previous corrective action.
 - Red - Problem, immediate corrective action required.
- (5) Draft status report completed by project manager; awaiting approval by agency head or sponsor.
- (6) CIO assessment of the project, based on Secretariat evaluation and PMD analysis.
- (7) Comments presented at most recent joint APA/PMD project review meeting.
- (8) Projects are listed in order of Life Cycle Phase and within each phase by Secretariat then Agency.
- (9) Date project granted Project Initiation Approval and entered Detailed Planning.
- (10) Date project completed Detailed Planning and entered Execution and Control.
- (11) Date project completed Execution and Control and entered Closeout.
- (12) Values noted in Project Proposal and Charter when granted Initiation Approval. Figure not available for some Pre-ITIB projects.
- (13) Current value reflecting any approved baseline changes. Variance from original value noted below the value.
- (14) Current date reflecting any approved baseline changes. Variance from original date noted below the date.
- (15) Planned and Actual Cost-to-Date figures based on agency and Commonwealth financial reporting, which can lag one or two months behind the project status reporting period.

Commonwealth of Virginia IT Projects Status Report for May 2019 - Part 1: Status and Assessment

| Secretariat & Agency (1) | Project Title (2) | Date & Ratings of Most Recent Agency Key Status Indicators (3,4) | | | | | CIO Assessment Rating (4,6) | Comments | | |
|--|---|--|--------------|--------------|--------------|--------------|-----------------------------|------------|--|--|
| | | Performance | Budget | Schedule | Scope | Risk | | APA (7) | CIO | |
| Projects in the Detailed Planning Phase | | | | | | | | | | |
| 1 | 188 Secretary of Health & Human Resources 720 Department of Behavioral Health and Developmental Services | DOJ - Licensing System | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-2 | Not under review at this time. | Project on track for schedule and budget. The CTP detail planning forms are under review for final approval. |
| 2 | 188 Secretary of Health & Human Resources 720 Department of Behavioral Health and Developmental Services | OneMind Cerner Millennium Replacement Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Project on track for schedule and budget. The project manager successfully delivered the detail planning documents on April 29th. |
| 3 | 190 Secretary of Finance 151 Department of Accounts | Cardinal Payroll | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | Yellow assessment due to scope, schedule and budget. Executive management and project teams are working together to ensure project success. Scope analysis phase is complete. Next steps for Cardinal HCM implementation is to finalize scope of work with DHRM, review project scope and implementation approach with system owners and review SOW documents with DHRM/DOA leadership. |
| Projects in the Execution and Control Phase | | | | | | | | | | |
| 4 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | End User Services Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-2 | Not under review at this time. | Yellow assessment due to schedule. A draft SSP has been conditionally accepted; however, the VAR is still in process for approval. Integrations with the MSI continue but are behind schedule. Connectivity to the ServiceNow test environment cannot occur until the VAR is approved. SMM and SPLM efforts continue, but are schedule challenged. Operating Level Agreements (OLAs) and other integration tasks are in progress, but have not been completed. |
| 5 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Managed Security Services Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Yellow assessment due to risk. There will be a change in project managers, and although the expectation is the new project manager will be appropriate for the project, there is the concern and risk of replacing a key role while the project is in execution. A change request to extend the project end date has been formally approved. The OLA with the MSI has been approved. The System Security Plan (SSP) has also been approved. |
| 6 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Messaging Services Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | The Internal Agency Oversight Committee (IAOC) voted to keep the project open in order to maintain visibility on the remaining items that need completion. The project team continues to work on outstanding items. The Incident Response Plan was given formal approval. The project is on track for completion by 12/31/19, however the dependency on Google to implement a required change may impact the end date of this project. |
| 7 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Multisourcing Service Integrator Services | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Red assessment due to schedule and risk. User Acceptance Testing (UAT), IT Financial Management (ITFM) integration and other supplier/tower integrations development/finalization continue behind schedule. Most of the SMM chapters have been approved, however OLAs and SLAs are not approved. The lack of schedule integration is impacting VITA's correct allocation of project resources. A change request to extend the project to August 31st has formally been approved. |
| 8 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Server/Storage Sourcing | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Yellow assessment due to schedule and risk. A draft SSP has been conditionally accepted; however, the VAR is still in process for approval. Integrations with the MSI continue but are behind schedule. Connectivity to the ServiceNow Test environment cannot occur until the VAR is approved. SMM and SPLM efforts continue, but are schedule challenged. Operating Level Agreements (OLAs) and other integration tasks are in progress, but have not been completed. |

| | | | | | | | | | | |
|----|--|---|--------------|--------------|--------------|--------------|--------------|------------|--|---|
| 9 | 184 Secretary of Technology 136 Virginia Information Technologies Agency | Network Voice and Video Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Significant progress has been made. Over 50% of the integration points with the MSI have been fully closed out. The 8 SPLM services were all submitted into the demand pipeline and half of them have approved VAR's. Requirements, design and development were completed for Incident eBonding. The change request extending the project to June 4th has been formally approved. |
| 10 | 185 Secretary of Education 207 University of Virginia | Academic Identity & Access Management (IAM) System | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Tier III School. The project is on track with major milestones and key status indicators. Project in closeout. |
| 11 | 185 Secretary of Education 207 University of Virginia | ResearchUVa Phase II | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Tier III School. The project is on track with major milestones and key status indicators. |
| 12 | 185 Secretary of Education 212 Virginia State University | Network Infrastructure Upgrade | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-2 | Not under review at this time. | Project is progressing for scope and schedule. New strategy requires a change control request for budget. Executive management and project teams are working well together to ensure project success. All risks and issues are being effectively managed. |
| 13 | 185 Secretary of Education 215 University of Mary Washington | Jepson Science Center Expansion - Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Tier II Project. The project is on track with major milestones and key status indicators. |
| 14 | 185 Secretary of Education 260 Virginia Community College System | Virginia Integrated Program of Planning and Advising (VIP-PASS) | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Tier II Project. The project is on track with major milestones and key status indicators. |
| 15 | 185 Secretary of Education 425 Jamestown-Yorktown Foundation | JS Exhibit Renovation Technology | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Project is progressing well for scope, schedule and budget. Executive management and project teams are working well together to ensure project success. Cortina Productions continues to be on track for completion of computer interactive, film and special effects deliverables. Gallery construction of the facility has begun and installation of the equipment will be a phased approach. Risks and issues are being managed effectively. |
| 16 | 186 Secretary of Transportation 154 Department of Motor Vehicles | Motor Carrier IFTA/IRP/CVIEW Solution | Mar 31, 2018 | Mar 31, 2018 | Mar 31, 2018 | Mar 31, 2018 | Mar 31, 2018 | Category-3 | Not under review at this time. | The project has missed some of the intermediate project task dates but is still on track to meet the June 30, 2019 closeout date. |
| 17 | 186 Secretary of Transportation 501 Department of Transportation | SMART SCALE - SMART Portal Enhancements Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | The project team has started gathering the final details for the last release on this contract and the project is on time to complete as planned. |
| 18 | 187 Secretary of Public Safety & Homeland Security 156 Department of State Police | E-Summons Pilot Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Green assessment (trending yellow) due to schedule. VSP has still not finalized a contract with Tyler Technologies; it's being held up with their legal department. Tyler has started to perform certain activities so as not to disrupt VSP's schedule. That's a good sign that the contract is close to being finalized. |
| 19 | 187 Secretary of Public Safety & Homeland Security 960 Department of Fire Programs | LMS Project VDFP | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Configuration efforts are almost done, testing is also almost completed, and the final data migration efforts are being planned for. Project is on schedule for a July rollout. |
| 20 | 187 Secretary of Public Safety & Homeland Security 999 Department of Alcoholic Beverage Control | ABC Financial System Replacement | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | Phase 1 deployed on schedule in March, "budgets" deployment was for Oracle's Enterprise Planning and Budgeting Cloud Service (EPBCS). Phase 2 deployment is still on schedule for June 2019, Oracle's Fusion ERP Cloud Application. |

| | | | | | | | | | | |
|----|--|---|--------------|--------------|--------------|--------------|--------------|------------|--|--|
| 21 | 187 Secretary of Public Safety & Homeland Security 999 Department of Alcoholic Beverage Control | ABC Licensing and Compliance System | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | Yellow assessment due to schedule. Testing and bug fixes continue to cause slight delays in the project schedule. Data conversion efforts are also behind schedule, however the project team is working with the enforcement team to prioritize license types to be converted, so as to perform the important license conversions first and leave the older, no longer active license conversions until later. This should enable the data migration to meet the existing schedule. The project manager left ABC and a new project manager was assigned. |
| 22 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Data Warehouse | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | MES Program component project. The team successfully rolled out Release 4 in April, which included FADS (Fraud Abuse Detection System) as well as MESISS Single Sign On facility. This is a major accomplishment for the EDWS team and the MES Program. Successive releases are currently in progress. Schedule and cost performance indices indicate project is on track. Project continues to be monitored very closely. Risks actively managed. |
| 23 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Encounter Processing | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | MES Program component project. Phase 2, Release 4 (Electronic Visit Verification (EVV)) of EPS is in development and progressing well. Team is deeply involved in data integration activities with sibling projects in the MES Program. Additional project scope is under consideration; an IAPDU is being drafted that will expand project scope and extend schedule and budget. The project is on track to deliver the revised scope. |
| 24 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Fee for Service and Core Processing | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | Green assessment (trending yellow) due to dependency risks. MES Program component project. The multiple work streams of the MCSS project have experienced different statuses during this period. The largest stream, OPSS/PLMS, continues to make strong progress. PRSS is fully engaged in project execution. Appeals, which has very few dependencies with other projects and work streams, is in discussions with a new vendor. Care Management is nearing contract finalization. Generally, MCSS is on a trajectory for scope, schedule and budget achievement, however as all of the MES Program components begin to require connections with each other, there is little contingency remaining for errors or delays. Monitoring closely. |
| 25 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Integration | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | Green assessment (trending yellow) due to cross dependency risks. MES Program component project. Project aggressively managing complex integration of MES functional modules and underlying technology. Single Sign On (SSO) successfully implemented for EDWS Fraud Detection functionality, which was a significant accomplishment. The baselined Integrated Master Schedule is the common reference point for all MES modules. The biggest risks continue to be the cross dependencies across multiple modules, and implementing the required end state network according to schedule. The team is working proactively with all modules to manage the risks. |
| 26 | 188 Secretary of Health & Human Resources 765 Department of Social Services | APECS Documents | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Red assessment due to no approved schedule or budget. The project manager submitted a new project schedule on April 23rd to establish a new baseline. PMD consultant concerns raised to senior management. |
| 27 | 188 Secretary of Health & Human Resources 765 Department of Social Services | CCWIS (Comprehensive Child Welfare Information System) - Mobility | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Not under review at this time. | Project on schedule and budget. Preliminary design presented to representatives of the local facility the week of April 16th with excellent feedback. |
| 28 | 188 Secretary of Health & Human Resources 765 Department of Social Services | DCSE Document Management Software Project | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-2 | Not under review at this time. | Red assessment due to resources. Project in crisis with no assigned project management or dedicated technical staff. The project was previously closed without completing full scope and acceptance criteria. The new agency executive staff has project under review. Weekly meetings are being held with stakeholders to review progress and options. |
| 29 | 188 Secretary of Health & Human Resources 765 Department of Social Services | Integration of Appeals Programs | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-2 | Not under review at this time. | Red assessment (trending yellow) due to pending change request with schedule and budget modification. Project was scheduled for completion in October 2018. Resources have been reassigned to complete project. |
| 30 | 190 Secretary of Finance 161 Department of Taxation | JBoss and VTOL Upgrade | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-3 | Not under review at this time. | Project is progressing well for scope, schedule and budget. Executive management, stakeholders and project teams are working well together to ensure project success. Risks and issues are being identified, tracked and managed effectively according to the project plan. Phase 1 (JBoss Upgrade) is complete. VTOL Phase 2 and 3 (Individual and Business Portals) are in progress. |

| | | | | | | | | | | |
|----------------------------------|---|--------------------------------------|--------------|--------------|--------------|--------------|--------------|------------|--|--|
| 31 | 192 Secretary of Commerce and Trade 182 Virginia Employment Commission | Unemployment Insurance Modernization | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-1 | Under review; APA concurs with PMD review. | Yellow assessment due to schedule. VEC7555 critical service request completed successfully 3/23/2019 and VEC is no longer operating on a single node. Project is on track with major milestones; however, the overall schedule needs adjustment and the vendor, HCL is late providing an updated schedule. |
| Projects under Suspension | | | | | | | | | | |
| 32 | 192 Secretary of Commerce and Trade 226 Board of Accountancy | VBOA Licensing System/Database | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Mar 31, 2019 | Category-2 | Under review; APA concurs with PMD review. | Project suspended (agency requested) due to risk and vendor turnover. Agency has requested project suspension to allow time to meet with the Board of Directors and determine if the contracted solution will meet agency needs. Current vendor, MicroPact was recently acquired by Tyler Technologies. |

Commonwealth of Virginia IT Projects Status Report for May 2019- Part 2: Baseline Report

| Secretariat & Agency (1) | Project Title (2) | CIO Assessment Rating | # of Baseline Changes (> 10%) | Life Cycle Phase (8) | | | Original Cost and Schedule Baselines (12) | | Current Cost and Schedule Baselines | | Most Recent Cost-to-Date (15) | | Notes | |
|--|---|--|-------------------------------|-----------------------|----------------------------|---------------|---|---------------------------------------|-------------------------------------|--|---------------------------------------|--------------|--------------|---|
| | | | | Detailed Planning (9) | Execution and Control (10) | Closeout (11) | Estimate at Completion | Planned Submission of Closeout Report | Estimate at Completion (13) | Planned Submission of Closeout Report (14) | Planned | Actual | | |
| Projects in the Detailed Planning Phase | | | | | | | | | | | | | | |
| 1 | 188 Secretary of Health & Human Resources 720 Department of Behavioral Health and Developmental Services | DOJ - Licensing System | Cat-2 | 0 | Nov 7, 2018 | | | \$2,761,323 | Apr 1, 2020 | No Change | No Change | \$627,931 | \$597,931 | |
| 2 | 188 Secretary of Health & Human Resources 720 Department of Behavioral Health and Developmental Services | OneMind Cerner Millennium Replacement Project | Cat-1 | 0 | Jan 17, 2019 | | | \$47,642,455 | Jan 30, 2021 | \$46,919,649 Variance -\$722,806 | No Change | \$12,209,382 | \$7,785,000 | Planned vs. actual cost variance due to delayed project start vendor invoices in process. |
| 3 | 190 Secretary of Finance 151 Department of Accounts | Cardinal Payroll | Cat-1 | 1 | Aug 24, 2016 | Oct 7, 2016 | | \$42,500,000 | May 30, 2019 | \$43,000,000 Variance \$500,000 | Jun 30, 2019 Variance 1 Months | \$39,712,037 | \$37,945,523 | Moved back to Detailed Planning Phase. |
| Projects in the Execution and Control Phase | | | | | | | | | | | | | | |
| 4 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | End User Services Project | Cat-2 | 0 | Jun 27, 2018 | Dec 19, 2018 | | \$5,827,187 | Mar 15, 2019 | No Change | Jun 15, 2019 Variance 3 Months | \$464,690 | \$163,566 | |
| 5 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Managed Security Services Project | Cat-1 | 0 | Dec 13, 2017 | Dec 13, 2018 | | \$3,296,446 | Oct 15, 2018 | No Change | Jun 15, 2019 Variance 8 Months | \$2,405,061 | \$2,035,245 | |
| 6 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Messaging Services Project | Cat-1 | 2 | Aug 3, 2016 | Jul 12, 2017 | | \$5,501,436 | Jun 30, 2017 | \$8,324,783 Variance \$2,823,347 | Dec 31, 2019 Variance 30 Months | \$7,970,430 | \$6,866,674 | Change requests approved by CIO January 2017, June 2017. |
| 7 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Multisourcing Service Integrator Services | Cat-1 | 1 | Jun 29, 2017 | Sep 19, 2018 | | \$20,100,000 | Feb 28, 2019 | No Change | Aug 31, 2019 Variance 6 Months | \$10,963,958 | \$10,222,032 | |
| 8 | 180 Secretary of Administration 136 Virginia Information Technologies Agency | Server/Storage Sourcing | Cat-1 | 0 | Jun 30, 2018 | Dec 11, 2018 | | \$10,766,537 | May 24, 2019 | No Change | Aug 23, 2019 Variance 3 Months | \$6,492,000 | \$3,351,400 | |
| 9 | 184 Secretary of Technology 136 Virginia Information Technologies Agency | Network Voice and Video Project | Cat-3 | 0 | Jul 30, 2018 | Dec 18, 2018 | | \$2,155,979 | Feb 4, 2019 | No Change | Jun 4, 2019 Variance 4 Months | \$218,000 | \$213,078 | |
| 10 | 185 Secretary of Education 207 University of Virginia | Academic Identity & Access Management (IAM) System | Cat-3 | 0 | | | | \$2,760,000 | Jun 30, 2019 | No Change | No Change | | | |

| | | | | | | | | | | | | | | |
|----|--|---|-------|---|--------------|--------------|--|--------------|--------------|-----------|---------------------------------------|--------------|--------------|---|
| 11 | 185 Secretary of Education 207 University of Virginia | ResearchUVa Phase II | Cat-3 | 0 | | | | \$2,950,000 | Jun 28, 2019 | No Change | No Change | | | |
| 12 | 185 Secretary of Education 212 Virginia State University | Network Infrastructure Upgrade | Cat-2 | 0 | Sep 7, 2018 | Apr 2, 2019 | | \$2,586,127 | Dec 2, 2021 | No Change | Jan 31, 2022 Variance 1 Months | \$417,000 | \$417,000 | |
| 13 | 185 Secretary of Education 215 University of Mary Washington | Jepson Science Center Expansion - Project | Cat-3 | 0 | | | | \$1,530,440 | Dec 31, 2018 | No Change | Jul 31, 2019 Variance 7 Months | \$94,040 | \$94,040 | |
| 14 | 185 Secretary of Education 260 Virginia Community College System | Virginia Integrated Program of Planning and Advising (VIP-PASS) | Cat-3 | 0 | | | | \$6,395,130 | Jul 30, 2019 | No Change | No Change | | | |
| 15 | 185 Secretary of Education 425 Jamestown-Yorktown Foundation | JS Exhibit Renovation Technology | Cat-3 | 0 | Nov 1, 2017 | Nov 1, 2018 | | \$2,833,457 | Apr 30, 2020 | No Change | No Change | \$1,942,441 | \$1,557,517 | |
| 16 | 186 Secretary of Transportation 154 Department of Motor Vehicles | Motor Carrier IFTA/IRP/CVIEW Solution | Cat-3 | 0 | Dec 29, 2017 | Oct 22, 2018 | | \$4,568,022 | Jun 30, 2019 | No Change | No Change | \$610,858 | \$628,488 | |
| 17 | 186 Secretary of Transportation 501 Department of Transportation | SMART SCALE - SMART Portal Enhancements Project | Cat-3 | 0 | Apr 11, 2017 | Jul 31, 2017 | | \$3,200,000 | Jul 31, 2019 | No Change | No Change | \$2,888,287 | \$2,844,198 | |
| 18 | 187 Secretary of Public Safety & Homeland Security 156 Department of State Police | E-Summons Pilot Project | Cat-1 | 0 | Nov 20, 2018 | May 2, 2019 | | \$1,613,146 | Nov 29, 2019 | No Change | No Change | \$17,000 | \$17,000 | |
| 19 | 187 Secretary of Public Safety & Homeland Security 960 Department of Fire Programs | LMS Project VDFP | Cat-1 | 0 | Jun 14, 2018 | Sep 5, 2018 | | \$452,250 | Aug 31, 2019 | No Change | No Change | \$313,000 | \$313,000 | |
| 20 | 187 Secretary of Public Safety & Homeland Security 999 Department of Alcoholic Beverage Control | ABC Financial System Replacement | Cat-1 | 0 | Jun 15, 2018 | Aug 24, 2018 | | \$23,700,000 | Oct 1, 2019 | No Change | Jun 30, 2019 Variance -4 Months | \$5,480,602 | \$5,669,777 | |
| 21 | 187 Secretary of Public Safety & Homeland Security 999 Department of Alcoholic Beverage Control | ABC Licensing and Compliance System | Cat-1 | 0 | Aug 28, 2017 | Feb 13, 2018 | | \$8,743,786 | Oct 30, 2020 | No Change | No Change | \$3,956,131 | \$3,502,136 | |
| 22 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Data Warehouse | Cat-1 | 0 | Dec 15, 2017 | Feb 14, 2018 | | \$27,572,362 | Feb 28, 2020 | No Change | Jul 2, 2020 Variance 5 Months | \$18,786,246 | \$13,399,618 | IAOC approved schedule change 1/9/18; scope & budget unchanged. |

| | | | | | | | | | | | | | | |
|----------------------------------|--|---|-------|---|--------------|--------------|--|--------------|--------------|--|---------------------------------------|--------------|--------------|--|
| 23 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Encounter Processing | Cat-1 | 1 | Aug 17, 2016 | Oct 18, 2016 | | \$8,000,000 | Sep 30, 2018 | \$9,489,009 Variance \$1,489,009 | Dec 31, 2019 Variance 15 Months | \$8,881,917 | \$6,413,702 | CIO approved scope, schedule and budget change 10/4/18. |
| 24 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Fee for Service and Core Processing | Cat-1 | 0 | Oct 13, 2017 | May 9, 2018 | | \$78,132,905 | Jan 31, 2020 | No Change | No Change | \$42,654,418 | \$35,709,314 | |
| 25 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Integration | Cat-1 | 0 | Oct 26, 2017 | Aug 3, 2018 | | \$26,707,463 | Mar 23, 2020 | \$27,571,704 Variance \$864,241 | Jun 26, 2020 Variance 3 Months | \$9,845,163 | \$9,330,617 | IAOC approved schedule and budget change (<10%). |
| 26 | 188 Secretary of Health & Human Resources 765 Department of Social Services | APECS Documents | Cat-3 | 0 | Jul 30, 2018 | Aug 27, 2018 | | \$374,500 | Jun 28, 2019 | No Change | No Change | \$450,000 | \$40,000 | |
| 27 | 188 Secretary of Health & Human Resources 765 Department of Social Services | CCWIS (Comprehensive Child Welfare Information System) - Mobility | Cat-1 | 0 | Aug 23, 2018 | Dec 10, 2018 | | \$2,445,636 | Nov 29, 2019 | No Change | No Change | \$1,029,082 | \$327,435 | |
| 28 | 188 Secretary of Health & Human Resources 765 Department of Social Services | DCSE Document Management Software Project | Cat-2 | 1 | Nov 9, 2016 | Sep 11, 2017 | | \$904,233 | Jan 31, 2017 | \$1,129,296 Variance \$225,063 | Jun 30, 2018 Variance 17 Months | \$1,137,296 | \$1,002,999 | |
| 29 | 188 Secretary of Health & Human Resources 765 Department of Social Services | Integration of Appeals Programs | Cat-2 | 0 | Jan 19, 2017 | Aug 2, 2018 | | \$549,830 | Aug 30, 2018 | No Change | No Change | \$549,830 | \$464,623 | |
| 30 | 190 Secretary of Finance 161 Department of Taxation | JBoss and VTOL Upgrade | Cat-3 | 0 | Feb 15, 2018 | Aug 1, 2018 | | \$998,552 | Aug 15, 2019 | No Change | Jul 15, 2020 Variance 11 Months | \$998,552 | \$363,128 | |
| 31 | 192 Secretary of Commerce and Trade 182 Virginia Employment Commission | Unemployment Insurance Modernization | Cat-1 | 5 | Sep 17, 2009 | Apr 8, 2011 | | \$58,831,331 | Sep 27, 2013 | \$69,713,259 Variance \$10,881,928 | May 19, 2020 Variance 80 Months | \$57,133,437 | \$57,029,154 | Change requests approved by CIO October 2011, September 2013, October 2015, May 2016, July 2017. |
| Projects under Suspension | | | | | | | | | | | | | | |
| 32 | 192 Secretary of Commerce and Trade 226 Board of Accountancy | VBOA Licensing System/Database | Cat-2 | 1 | Oct 23, 2017 | May 2, 2018 | | \$860,468 | Nov 30, 2018 | \$990,845 Variance \$130,377 | Dec 31, 2019 Variance 13 Months | \$381,592 | \$378,135 | Change request approved by CIO June 2018. |

Commonwealth of Virginia IT Projects Status Report for May 2019 - Part 3: Projected Initiation

| | Secretariat & Agency (1) | Project Title (2) | Project Description | Estimated | | | Notes |
|---|--|--|--|--------------|--------------|--------------|-------|
| | | | | Start Date | End Date | Total Cost | |
| 1 | 185 Secretary of Education 212 Virginia State University | Implement Banner XE Project | This project will upgrade the current Banner ERP system and modules to the latest version. | Jun 7, 2019 | Nov 30, 2020 | \$1,000,000 | |
| 2 | 187 Secretary of Public Safety & Homeland Security 799 Department of Corrections | Inmate Phone & Tablet Services Project | RFP to have a company install and maintain an IT network that would enable the DOC offenders to place telephone calls, in addition to offenders utilizing kiosks and tablets for services such as learning, training, scheduling, commissary ordering, banking, secured messaging, music, law library, and Ebooks. This contract will be for the period of seven years. The Virginia Department of Corrections (VADOC) has developed a coordinated strategy between the executive management, operations and the Corrections Technology Services Unit (CTSU) to support the increase needs of offender technology. Offender technology needs and solutions have come a long way in the past decade and this document establishes a strategy to be supported by executive leadership in the department. CTSU is continuously looking to support the vision statement "to be a progressive and proven innovative leader in the profession". Due to the continually increasing utilization of offender technology, CTSU can support the vision of the agency to leverage these systems in the pursuit of automating common administrative tasks while maintaining the required safety and security. In the correctional world, a recent goal of offender technology is to move administrative tasks away from the facility staff and have them performed (at least partially) by the offender. Examples include, but are not limited to: learning, training, scheduling, commissary ordering and banking, secured messaging, music, law library, Ebooks, creating a grievance, accepting a disciplinary charge, checking on classification status or release dates. Recent technological developments in mobile devices and wireless technologies have made it possible for such devices to be introduced safely within correction facilities and used not only by the correctional officers but also by the offenders themselves. These devices will deliver a self-service platform that the offender will leverage to do many tasks. | Sep 12, 2019 | Sep 23, 2020 | \$10,250,000 | |
| 3 | 188 Secretary of Health & Human Resources 602 Department of Medical Assistance Services | MES Financial Management | This is a component project within the DMAS MES Program. The MES Financial Management RFP addresses many of the financial business requirements that will comprise the MES solution, as mandated by CMS through the MITA 3.0 Framework. The project will deliver: Accounts Receivable Management, Accounts Payable Management, Fiscal Management, Payment and Reporting (limited). The DMAS MES FMS project management team will facilitate the transition from the current IT environment, which consists of VAMMIS financial transaction processes, Oracle Financials, and other internal systems. The future Financial Management System will be a contractor provided COTS or SaaS solution that aligns with the MITA 3.0 Framework, the CMS Seven Conditions and Standards. DMAS recognizes that the MITA Seven Conditions and Standards must be adhered to in order to be eligible for enhanced match funding. The CMS MITA Seven Standards and Conditions include system modularity, MITA maturity, HIPAA, accurate and timely processing, program evaluation and continuous improvement, enable interoperability with health care information systems, and leverage/reuse processes, systems, and other resources with other states as needed. | Jun 12, 2019 | Jul 31, 2020 | \$5,000,000 | |
